



PENREN this Week

February 24, 2003



Pentagon Secure Bypass/ Route 110 Project



Work resumes February 25, 2003



Snow removal activities will be completed on February 24. Regular construction activities on the RGS project will resume on Tuesday, February 25.



The PAC will replace the existing 58-year-old Pentagon Athletic Facility with a 127,000-square-foot facility that meets membership fitness and readiness needs.



Waterproofing has begun on the Mall Terrace.

Foundation Installation Continues.

Workers are continuing the preparation work on columns for the Mezzanine structure.




Wedges 2-5 Renovation

Wedges 2 through 5 encompass the remaining 4.5 million square feet of Pentagon space to be renovated by 2010.



Glass curtain wall panels being installed on the AE Drive Pedestrian Bridge at Corridor 4.5.

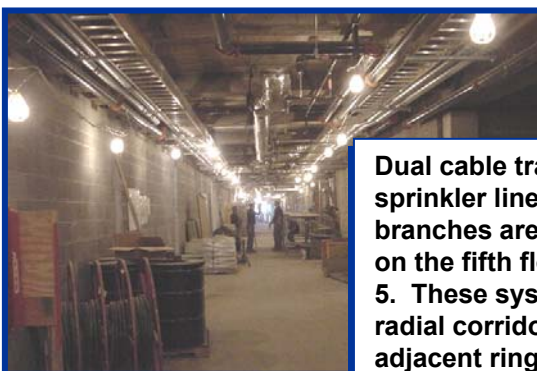

Dual cable trays, conduit, sprinkler lines and air branches are being installed on the fifth floor of Corridor 5. These systems serve the radial corridor and its adjacent rings.



The Wedge 2 Quality Assurance and Quality Control Inspectors continue performing their weekly Short Interval Production Schedule (SIPS) inspection walk-thrus.

For More Information on the
Pentagon Renovation Program,
visit our web site.

<http://renovation.pentagon.mil>
<http://renovation.pentagon.mil>

Questions & Comments
703 697-4357
