Pentagon Renovation SIPS Schedule
Excluding ADP Areas

9/26/2002

CONSTRUCTION

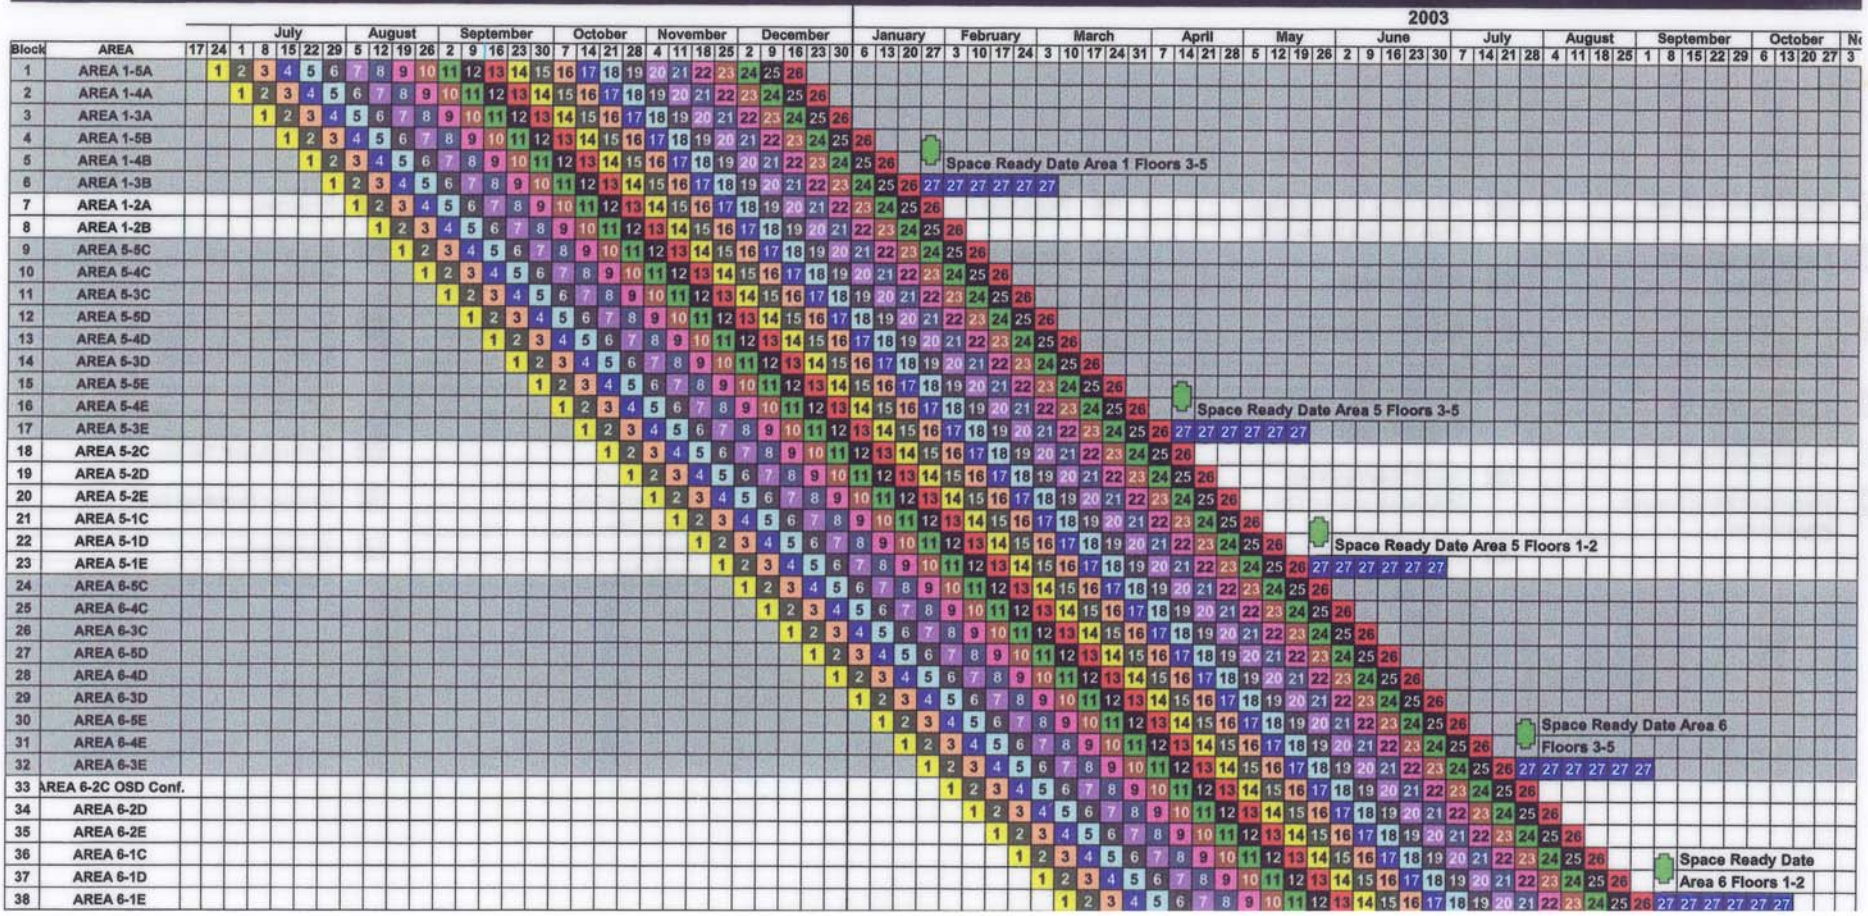

1	Sprinkler Mains/Branch Lines
2	Induction Boxes & Ductwork Fintube Piping
3	Outside Air Branch Duct FPIU Piping Connections
4	FPIU Piping Mains & Test
5	Mechanical Pipe/Duct Insulation
6	Frame/Drywall B-Zone Bulkheads Frame Columns
7	Frame A-Zone Walls & Bulkheads Frame Columns & Exterior Walls
8	PDS Cable Conduit
9	O/H Electrical & Wall Rough
10	Pull Power Wire Pull Control Wiring - JCI Rough-In Inspections - Walls
11	Insulate Walls/Vapor Barrier Wall Close-In Inspection (QA)
12	Hang Drywall on Walls & Soffits
13	Tape & Finish Walls & Soffits
14	Prime & Paint Walls & Ceilings
15	Install Smart Walls
16	Pull Comm & Data Wire - IM&T
17	IM&T Trim / Smart Wall Wire FPIU Startup EMCS Above Ceiling Point Checkout
18	Install Grid Window Trim
19	Mechanical Diffusers Cut Fire Sprinkler Drops Hang Lights Security Eqpt & Cable - Radian Rough-In Inspections - O/H DIA / Tenant Security / Close-In Inspection
20	Install Ceiling Tile Doors & Hardware Expansion Joints
21	EMCS Trim - JCI Fire Protection Trim Electrical Trim HVAC Trim Security Trim
22	Carpet/Base
23	Demountable Walls Window Blinds
24	Pre-Accreditation Walk-thru - DIA Final Inspection / Punchlist Final Paint Test & Balance
25	Furniture & Smart Wall Trim - OGC
26	Clean-Up / Space Ready Date
27	Commissioning Final Accreditation / Space Lockdown - DIA
